




F/A -18 UPC Integration with JC1 0.1

Justin Ennis




F/A-18 UPC Roadmap

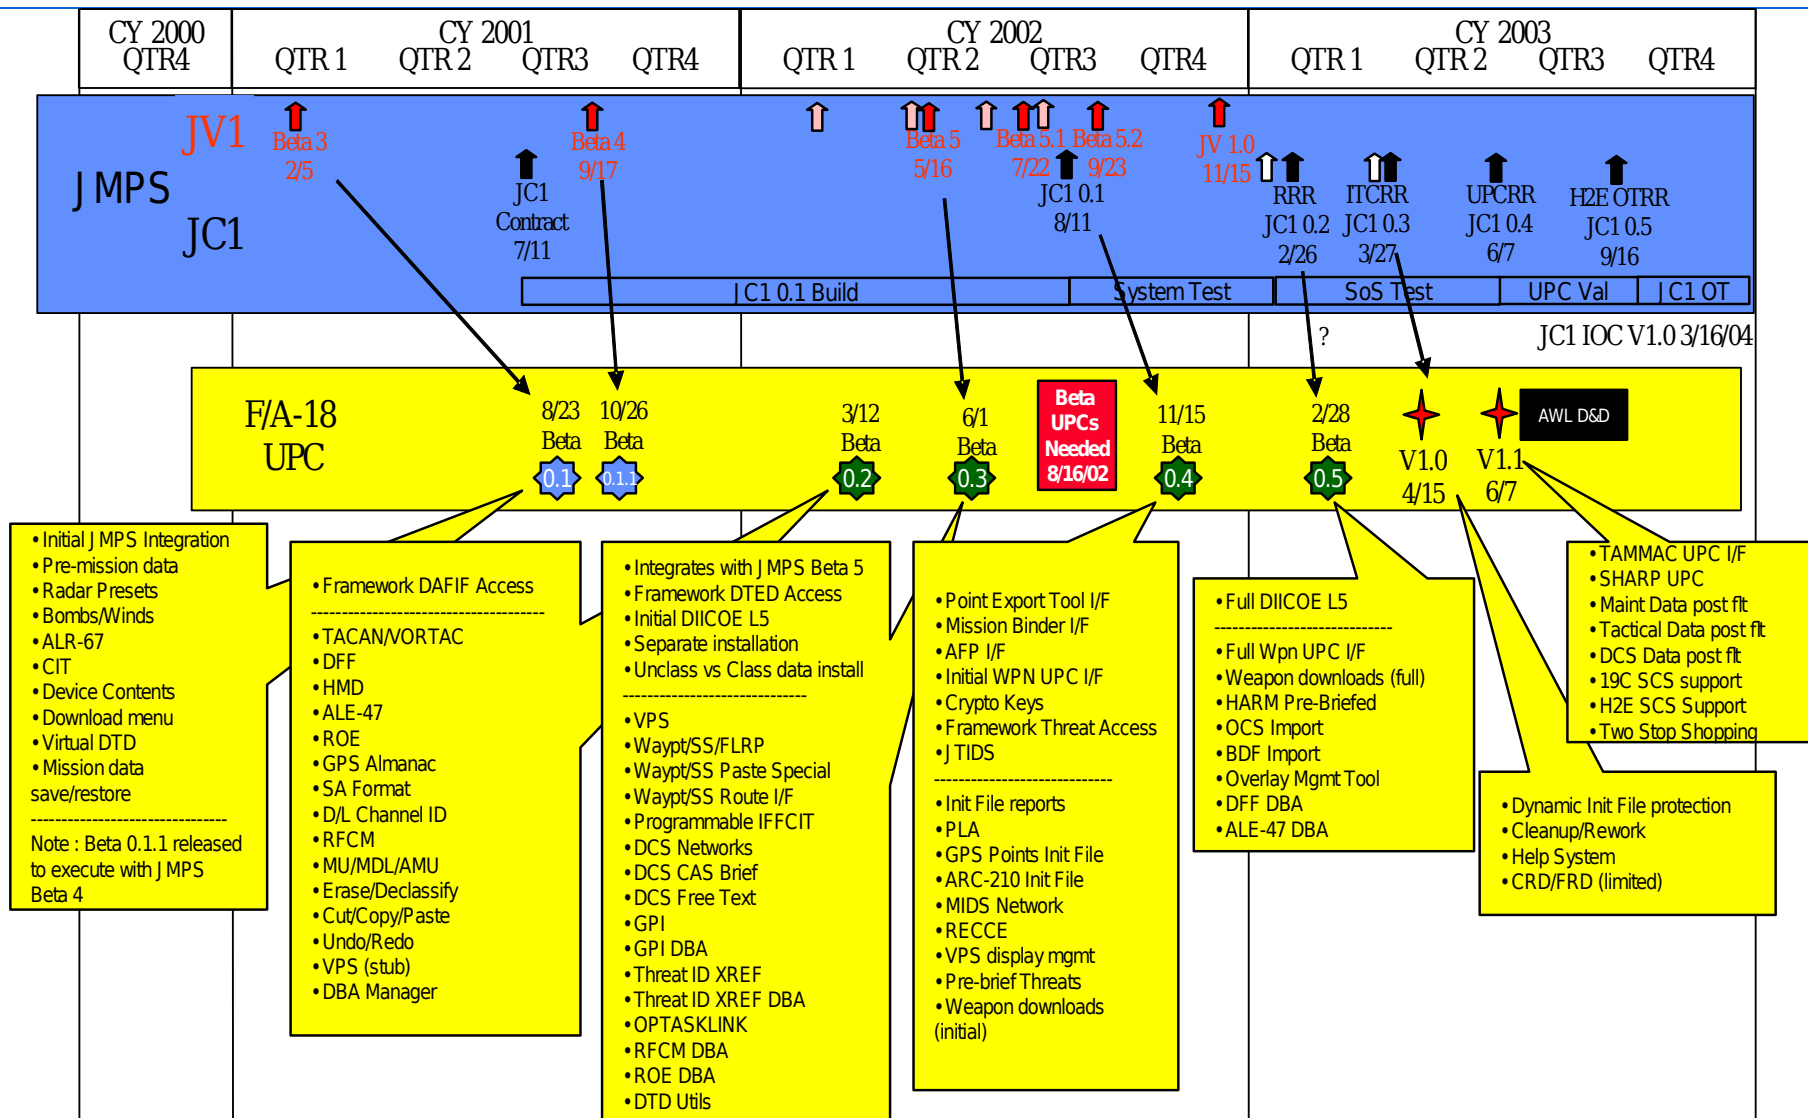




UPC Beta 0.4 Schedule





UPC Beta 0.5 Schedule





F/A-18 UPC Beta 0.4 AWL Test Schedule

ID	Task Name	Nov 10, '02							Nov 17, '02							Nov 24, '02							Dec 1, '02							Dec
		M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	S
59	UPC Beta 0.4 SRB																													
60	UPC Beta 0.4 AWL Test																													
61	TAC RECCE INIT file																													
62	MIDS terminal/network INIT file																													
63	Pre-briefed threats INIT file																													
64	Pre-briefed points, areas, lines INIT file																													
65	ARC-210 INIT file																													
66	MU/MDL/AMU download operation																													
67	Global Positioning System (GPS) support database																													

11/15
UPC Beta 0.4 SRB

UPC Beta 0.4 AWL Test
11/25

2.13 days

6 hrs

Tom Miller

2 hrs

Mary Kus

7 hrs

Mary Kus

8 hrs

Mary Kus

10 hrs

Mike Thompson

10 hrs


Tim Worley[50%]

1 hr

John Hemond



F/A-18 UPC Beta 0.5 AWL Test Schedule

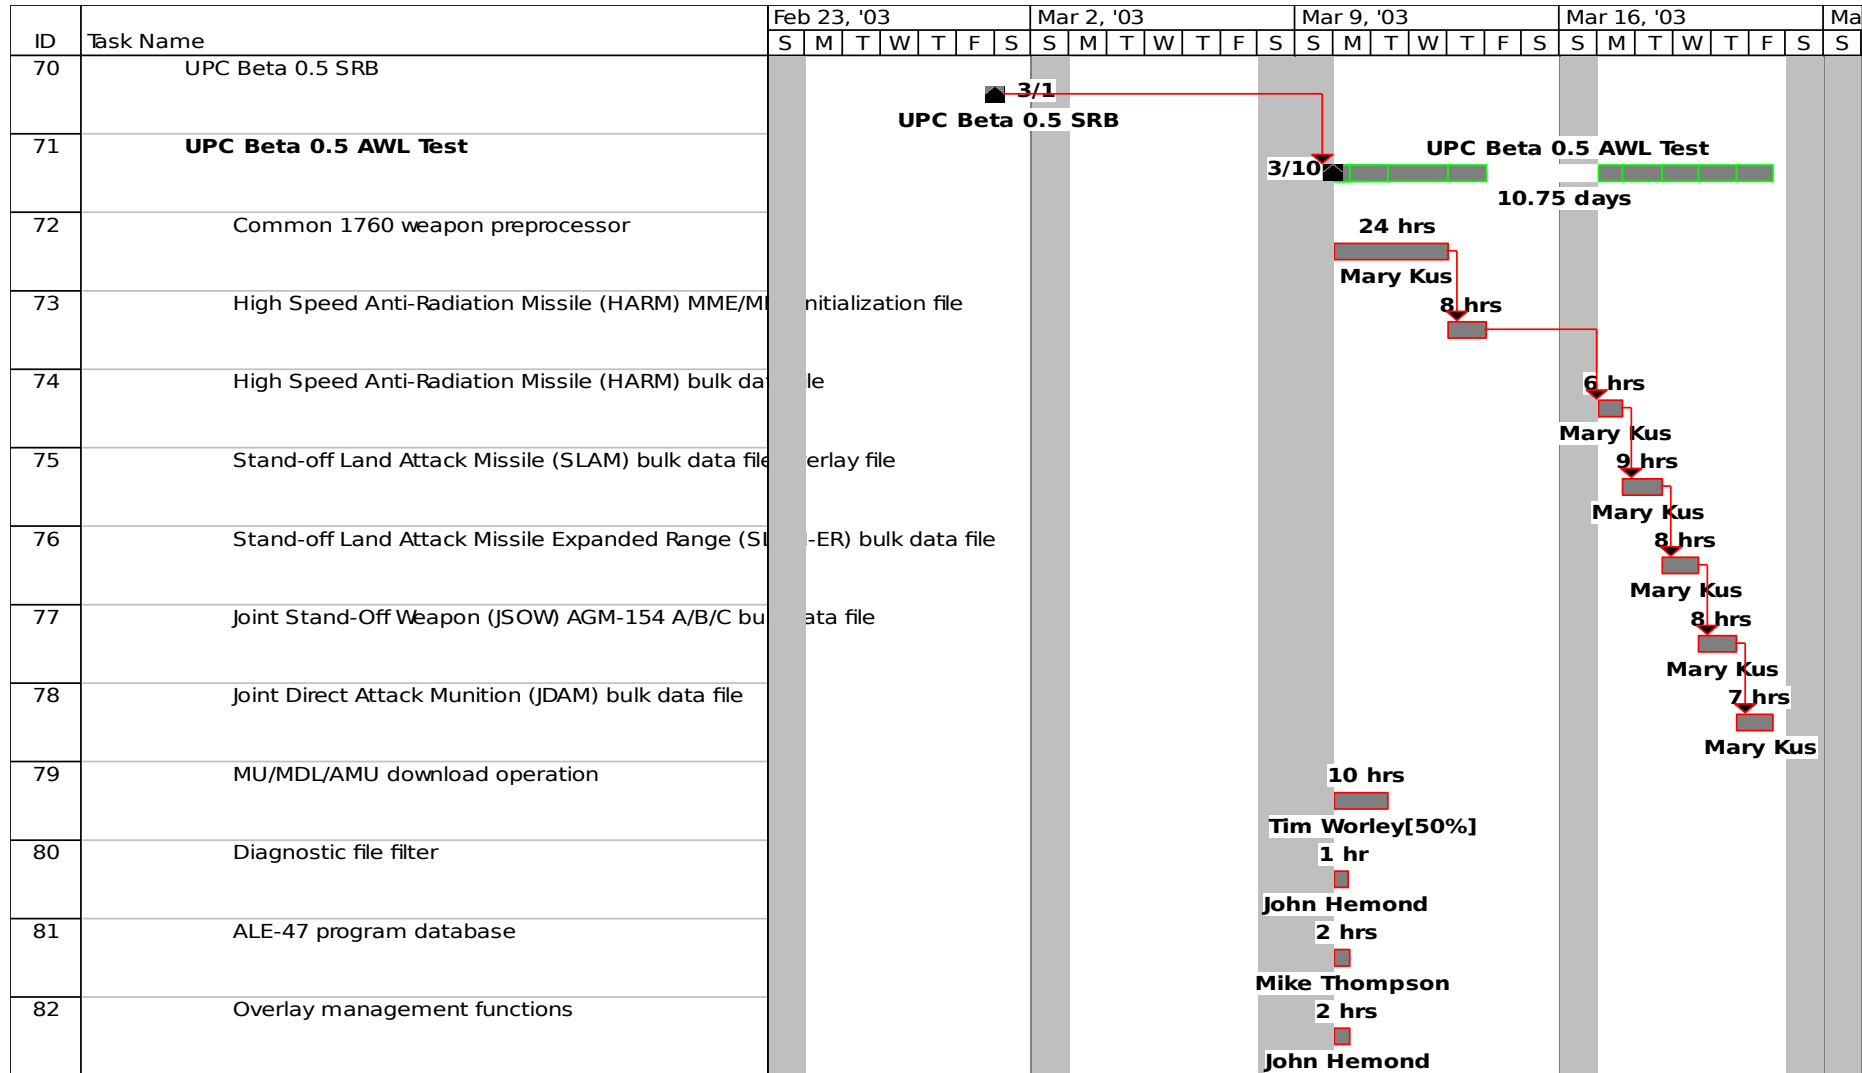



F/A-18 UPC JC1 0.1 Dependencies

- Mission Binders
 - Problems with development of Relocation Component may be exacerbated by lack of Programmer's Guide
- Water Pages

We prefer Programmer's Guide or Source Code to solve problems encountered with these components. Our backup plan is to utilize the Help Desk.
